

示识号	任务模式	任务名称	工期	开始时间	完成时	间	前置任务	资源名称
1	*	启动	5 个工作日	2020年11	月9日 2020:	年11月13日		
2	-5	启动核心团队	1 个工作日	2020年11月	∃9日 20204	∓11月9日		项目经理,UI专家
3	-5	干系人分析	1 个工作日	2020年11月	月9日 2020年	∓11月9日		项目经理
4	- 5	里程碑计划	1 个工作日	2020年11月	月9日 2020年	∓11月9日		项目经理
5	-9	制定项目章程	1 个工作日	2020年11	月12日 2020年	∓11月12日	2,3,4	项目经理
6 ===	-9	项目启动大会	1 个工作日	2020年11)	月13日 2020年	丰11月13日	5	项目经理,需求专家
7	*	规划						
8	-9	规划范围	4 个工作日	2020年11	月30日2020:	年12月3日		
9 ===	• =5	制定需求说明书	1 个工作日	2020年11月	月30日 2020年	≢11月30日	6	需求专家
10 ===	• =5	界面设计	1 个工作日	2020年12月	月1日 2020年	₹12月1日	9	UI专家
11 🥬	-5	详细设计说明书	1 个工作日	2020年12月	月1日 2020年	₹12月1日	9	设计专家
12	-5	项目范围说明书	1 个工作日	2020年12月	月1日 2020年	₹12月1日	9	项目经理
13	-5	创建WBS	1 个工作日	2020年12月	月2日 2020年	₹12月2日	10,11,12	项目经理
14	-5	形成范围基准	1个工作日	2020年12月	13日 2020年	三12月3日	13	项目经理
15	-5	规划时间	5 个工作日	2020年12月	4日 2020年	12月10日		
16	-5	排列工作包顺序	1个工作日	2020年12月	14日 2020年	三12月4日	14	项目经理
17	-5	估算资源	1个工作日	2020年12月	17日 2020年	三12月7日	16	项目经理
18		估算持续时间	1个工作日	2020年12月	18日 2020年	三12月8日	17	项目经理
19	-5	指定进度计划	1个工作日	2020年12月	19日 2020年	三12月9日	18	项目经理
20	-5	形成进度基准	1个工作日	2020年12月		三12月10日	19	项目经理
21	-5	规划成本	3 个工作日	2020年12月	11日 2020年	12月13日		
22	-5	项目成本估算	1个工作日	2020年12月	11日 2020年	三12月11日	20	项目经理
		Task		Inactive Summary		External T	asks	
		Split		Manual Task		External N	/lilestone	\Diamond
		Milestone	♦	Duration-only		Deadline		•
,	戈 粒体基因组》			Manual Summary Rollup		Progress		
Date: 202	20年12月9日	Project Summary		Manual Summary		Manual P	rogress	
		Inactive Task		Start-only	[- manadi i	9 55	
		Inactive Milestone	\Diamond	Finish-only	3			
				Page 1				

标识号	6	任务模式	任务名称	R	工期	开始时间		完成时间	前置任务	资源名称
23	ĭ	-5	项	目预算	1个工作日	2020年1	2月12日	2020年12月1	2日 22	项目经理
24	ŧ	-5	形	成范围基准	1个工作日	2020年12	2月13日	2020年12月1	3日 23	项目经理
25		-9	规划	质量	2个工作日	2020年1	2月4日	2020年12月7	' B	
26		-9	制	定测试计划	1个工作日	2020年12	2月4日	2020年12月4	日 14	质量专家
27		9	制	定测试用例	1个工作日	2020年12	2月7日	2020年12月7	日 26	质量专家
28		-5	规划	人力资源	2个工作日	2020年1	2月8日	2020年12月9	H	
29	ŧ	-9	制	定人力资源计划	1个工作日	2020年1		2020年12月8	日 17	项目经理
30	ŧ	-5	制	定人员配备管理计划	1个工作日	2020年1	2月9日	2020年12月9	日 29	项目经理
31		-5	规划	沟通	1个工作日	2020年1		2020年12月1		
32	ŧ	-5		定沟通管理计划	1个工作日	2020年1		2020年12月1	• •	项目经理
33		-9	规划		2个工作日	2020年1		2020年12月9		
34	Ť	-9		制外购分析	1个工作日	2020年12		2020年12月8		项目经理
35	Ť	-9		定采购文件	1个工作日	2020年1		2020年12月9		项目经理
36	_	-9		风险	3 个工作日	2020年1		2020年12月1		
37	İ	-9		别风险	1个工作日	2020年12		2020年12月1		1 11 1
38		-9		险分析	1个工作日	2020年1		2020年12月1	1 1	项目经理
39		-5		定风险登记册	1个工作日	2020年1		2020年12月1	* *	项目经理
40		-5	规划		1个工作日	2020年1		2020年12月1		项目经理
41		-5	执行与		13 个工作日	2020年1		2020年12月1		
42	•	-5		项目团队	1个工作日	2020年1		2020年11月3	• •	项目经理,测试员
43		-5	项目		10 个工作日	2020年1		2020年12月1		
44		-5	用	户模块 	6 个工作日	2020年1	2月1日	2020年12月8	B	
				Task		Inactive Summary		Ext	ernal Tasks	
				Split		Manual Task		Ext	ernal Milestone	\Diamond
				Milestone	>	Duration-only		De	adline	•
,		立体基因组注	E释 .mp	Summary	——	Manual Summary Rol	lup	Pro	ogress	
Date: 7	2020 ¹	年12月9日		Project Summary		Manual Summary		Ma	inual Progress	
				Inactive Task		Start-only	Е			
				Inactive Milestone		Finish-only	3			
						Page 2				

示识号	0	任务模式	任务名称	R	工期		开始时间		完成时间		前置任务	j	资源名称	
45	ĭ	-5		注册登录	2 个工作日		2020年12	月1日	2020年12	月2日	42		程序员1	
46	ŧ	5		首页	1个工作日		2020年12	月3日	2020年12	月3日	45		程序员1	
47	ŧ	5		输入内容	2个工作日		2020年12	月4日	2020年12	月7日	46		程序员2	
48		-5		查看结果	1个工作日		2020年12	月8日	2020年12	月8日	47		程序员2	
49		-5	管	理员模块	3 个工作日		2020年11	月30日	2020年12	月2日				
50	i	-5		审核注册用户	1个工作日		2020年11	月30日	2020年11	月30日			测试员1	
51	i	-5		用户数据库管理	2个工作日		2020年11	月30日	2020年12	月1日			程序员1,科	呈序员2
52	i	-5		基因数据库管理	3个工作日		2020年11	月30日	2020年12	月2日			程序员1,科	呈序员2
53	ŧ	-5		审核商家广告	1个工作日		2020年12	月1日	2020年12	月1日	62		项目经理	
54	ŧ	-5		播放广告	1个工作日		2020年12	月1日	2020年12	月1日	62		测试员1,测	训试员2
55		-5	内	部实现模块	10 个工作日		2020年11	月30日	2020年12	月11日				
56	ŧ	-		收集数据	2个工作日		2020年11	月30日	2020年12	月1日			需求专家	
57	ŧ	-		数据过滤	2个工作日		2020年12	月2日	2020年12	月3日	56		程序员1	
58	ŧ	-5		基因组装	2个工作日		2020年12	月4日	2020年12	月7日	57		程序员2	
59		-5		基因注释	2个工作日		2020年12	月8日	2020年12	月9日	58		程序员1	
60		-5		基因可视化	2个工作日		2020年12	月10日	2020年12	月11日	59		程序员2	
61		-	商	家模块	1个工作日		2020年11	月30日	2020年11	月30日				
62	ŧ	-		发布广告	1个工作日		2020年11	月30日	2020年11	月30日			测试员1	
63		*	项目	监控	12 个工作日		2020年12	月1日	2020年12	月14日				
64	ŧ	-5	各	项指标监控	7个工作日		2020年12	月1日	2020年12	月9日	42		测试员1,项	可目经理
	Ⅲ †	-5	监	控评审	4个工作日		2020年12	月10日	2020年12	月13日	64		设计专家,	项目经理
66	III	-5	变	更评审	1个工作日		2020年12	月14日	2020年12	月14日			设计专家,	项目经理
				Task		Inactive :	Summary			External T	asks			
				Split		Manual ⁻	•			External N	/lilestone	\Diamond		
				Milestone	♦	Duration				Deadline		•		
,		体基因组注	E释 .mp	Summary			Summary Rolli	JD QL		Progress				
Date: 2	2020年	三12月9日		Project Summary			Summary			Manual P	roaress			
				Inactive Task		Start-onl	•	[manual F	1091033			
				Inactive Milestone	\Diamond	Finish-or	•]						
							Page 3							

标识号	0	任务模式	任务名称	工期	开始时间	完成时间	前置任务	资源名称
67		-5	管理干系人	6 个工作日	2020年12月1日	2020年12月8日		
68	ŧ	-5	发布项目信息	6个工作日	2020年12月1日	2020年12月8日	42	项目经理
69	Ť		报告监控指标	5 个工作日	2020年12月1日	2020年12月7日	42	项目经理
70	ŧ	-5	干系人沟通	6个工作日	2020年12月1日	2020年12月8日	42	项目经理
71		-5	团队建设	2个工作日	2020年11月30日	2020年12月1日		
72	ŧ	-	培训	1个工作日	2020年12月1日	2020年12月1日	42	UI专家,测试员1,测
73	ŧ	-5	娱乐活动	1个工作日	2020年12月1日	2020年12月1日	42	UI专家,测试员1,测
74	ŧ	-5	沟通	1个工作日	2020年12月1日	2020年12月1日	42	UI专家,测试员1,测
75	ŧ		采购	1个工作日	2020年11月30日	2020年11月30日		需求专家
76	Ⅲ ┆		项目验收	1个工作日	2020年12月12日	2020年12月12日	43	UI专家,设计专家
77		*	收尾	7个工作日	2020年12月8日	2020年12月14日		
78			项目终验	1个工作日	2020年12月8日	2020年12月8日		UI专家,设计专家
79	ŧ		项目采购	1个工作日	2020年12月13日	2020年12月13日	76	项目经理
80		-5	项目内部收尾	2个工作日	2020年12月13日	2020年12月14日	76	UI专家,测试员1,测



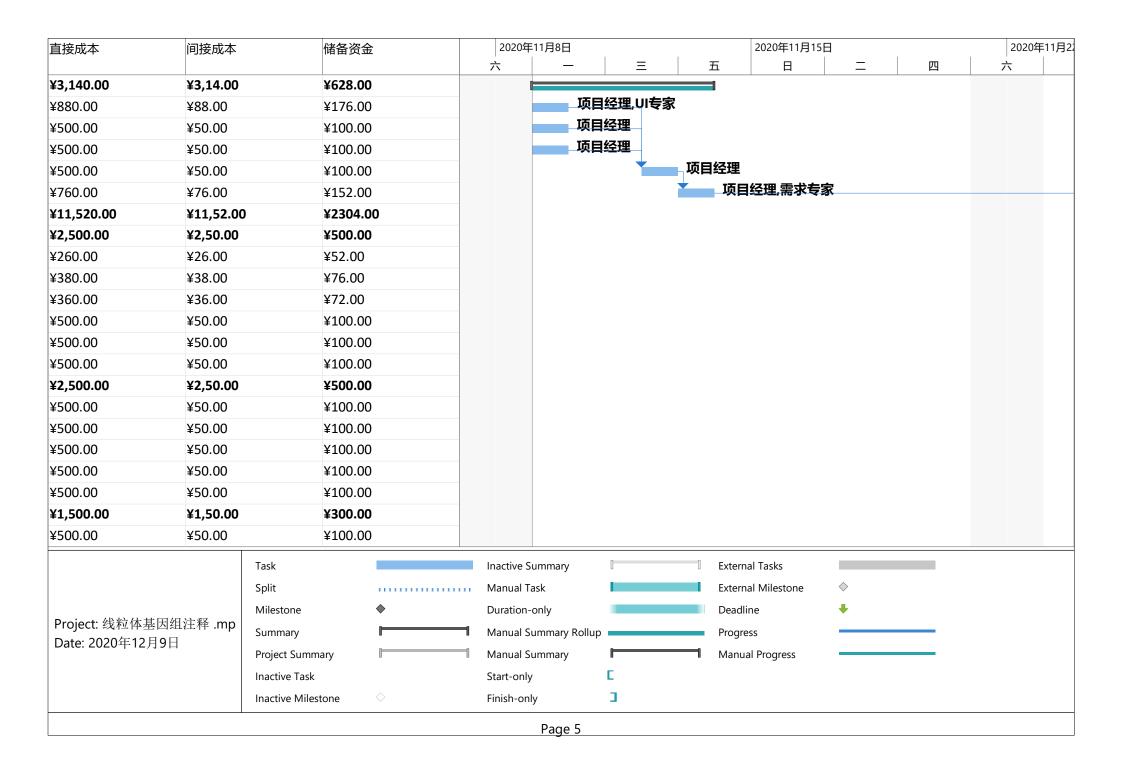

直接成本	间接成本	储备资金	金	2020年11月]8日			2020年11月15	3	2020				
				六	_	Ξ	五	日	=	四	六			
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥520.00	¥52.00	¥104.0	0											
¥260.00	¥26.00	¥52.00												
¥260.00	¥26.00	¥52.00												
¥1,000.00	¥1,00.00	¥200.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥1,000.00	¥1,00.00	¥200.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥1,500.00	¥1,50.00	¥300.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥500.00	¥50.00	¥100.0	0											
¥28,580.00	¥28,58.00	¥5716.	00											
¥760.00	¥76.00	¥152.0	0											
¥11,130.00	¥11,13.00	¥2226.	00											
¥2,460.00	¥2,46.00	¥492.0	0											
		Task		Inactive Sumr	nary		Extern	al Tasks						
		Split		Manual Task			Extern	al Milestone	\Diamond					
		Milestone	♦	Duration-only	<i>'</i>		Deadl	ine	•					
Project: 线粒体基		Summary		Manual Sumn			Progre	ess						
Date: 2020年12月	9日	Project Summary		Manual Sumn			_	al Progress						
		Inactive Task		Start-only		С								
		Inactive Milestone	\Diamond	Finish-only		3								
				D	age 6									

1500.00		间接成本	储备资金	È	2020年	11月8日			2020年11月15	日		2020年11月
100					六	_	Ξ	五	日	=	四	六
1710.00 17	¥820.00	¥82.00	¥162.00									
#30.00 ¥43.00 ¥86.00	¥500.00	¥50.00	¥100.00									
4,930.00	¥710.00	¥71.00	¥142.00									
260.00 ¥26.00 ¥52.00	¥430.00	¥43.00	¥86.00									
1,530.00	¥4,930.00	¥4,93.00	¥986.00									
22,130.00	¥260.00	¥26.00	¥52.00									
1500.00 150.00 150.00 100.00	¥1,530.00	¥1,53.00	¥306.00)								
10.00 10	¥2,130.00	¥2,13.00	¥426.00)								
3,48.00	¥500.00	¥50.00	¥100.00)								
420.00	¥510.00	¥51.00	¥102.00									
1820.00 ¥82.00 ¥164.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥142.00 ¥1408.00 ¥14	¥3,480.00	¥3,48.00	¥796.00									
#71.0.0	¥420.00	¥42.00	¥840.00)								
Froject: 线粒体基因组注释 .mp	¥820.00	¥82.00	¥164.00									
# 10.00	¥710.00	¥71.00	¥142.00									
Yeb	¥820.00	¥82.00	¥162.00									
#26.00	¥710.00	¥71.00	¥142.00									
#7,04.00	¥260.00	¥26.00	¥52.00									
Yes ¥260.00	¥26.00	¥52.00										
#2,54.00 ¥2,54.00 ¥508.00 ¥172.00 External Tasks Project: 线粒体基因组注释 .mp Date: 2020年12月9日 Project Summary Pr	¥7,040.00	¥7,04.00	¥1408.0	0								
External Tasks Split Milestone Duration-only Date: 2020年12月9日 Task Split Manual Summary Rollup Project Summary Inactive Task Start-only Inactive Milestone Finish-only Finish-only Summary Finish-only Summary Finish-only Summary Finish-only External Tasks External Milestone External Tasks External Milestone Manual Summary Frogress Manual Progress Manual Progress Finish-only Start-only Start-only Start-only Start-only Start-only Start-only Manual Summary Manual Progress	¥3,640.00	¥3,64.00	¥728.00									
Task Inactive Summary External Tasks Split Manual Task External Milestone ◆ Duration-only Deadline Summary Manual Summary Rollup Progress Project Summary Inactive Task Start-only Inactive Milestone ◆ Finish-only Inactive Milestone ◆ Finish-only Inactive Milestone ◆ Finish-only Inactive Milestone ◆ Finish-only Inactive Milestone ▼ Finish-only Inactive Mileston	¥2,540.00	¥2,54.00	¥508.00									
Project: 线粒体基因组注释 .mp Date: 2020年12月9日 Split Milestone Summary Project Summary Inactive Task Inactive Milestone Split Manual Task Duration-only Manual Summary Rollup Manual Summary Manual Summary Manual Summary Inactive Milestone Finish-only External Milestone Progress Manual Progress Inactive Milestone	¥860.00	¥86.00	¥172.00									
Project: 线粒体基因组注释 .mp Date: 2020年12月9日 Split Milestone Summary Project Summary Inactive Task Inactive Milestone Split Manual Task Duration-only Manual Summary Rollup Manual Summary Manual Summary Manual Summary Inactive Milestone Finish-only External Milestone Progress Manual Progress Inactive Milestone			Task		Inactive Su	ımmary		Exte	ernal Tasks			
Project: 线粒体基因组注释 .mp Date: 2020年12月9日 Milestone Summary Project Summary Project Summary Inactive Task Inactive Milestone Milestone Duration-only Manual Summary Rollup Manual Summary Froject Summary Inactive Milestone Finish-only Deadline Progress Manual Progress Inactive Milestone			Split		Manual Ta	sk		Exte	ernal Milestone	\Diamond		
Project: 线粒体基因组注释 .mp Date: 2020年12月9日 Project Summary Project Summary Progress Inactive Task Inactive Milestone Manual Summary Rollup Manual Summary Manual Summary E Inactive Milestone Finish-only Progress Manual Progress Inactive Milestone				♦	Duration-c	only		Dea	adline	•		
Date: 2020年12月9日 Project Summary Manual Summary Manual Progress Inactive Task Start-only Inactive Milestone Finish-only	•		Summary		Manual Su	mmary Rollup)	Pro	gress			
Inactive Task Start-only Inactive Milestone Finish-only	Date: 2020年12月	9⊟	Project Summary									
Inactive Milestone Finish-only						•	С		J			
Page 7				\Diamond		′	3					
						Page 7						

直接成本	间接成本	储备资金	2020年	F11月8日			2020年11月15	日		2020年11月2		
			六	_	≡	五	日	=	四	六		
¥5,980.00	¥5,98.00	¥1196.00										
¥2,100.00	¥2,10.00	¥420.00										
¥1,780.00	¥1,78.00	¥356.00										
¥2,100.00	¥2,10.00	¥420.00										
¥2,930.00	¥2,93.00	¥586.00										
¥890.00	¥89.00	¥178.00										
¥890.00	¥89.00	¥178.00										
¥890.00	¥89.00	¥178.00										
¥260.00	¥26.00	¥52.00										
¥740.00	¥74.00	¥148.00										
¥2,690.00	¥2,69.00	¥538.00										
¥740.00	¥74.00	¥148.00										
¥500.00	¥50.00	¥100.00										
¥1,450.00	¥1,45.00	¥290.00										

